



Ronald McDonald
House Charities®
Atlantic

Construction Progress Report

March 2024

Recent Highlights



- Approx. 99% of project trades tendered and awarded; Less than 1% yet to be tendered.
- Concrete structure is completed.
- As with many construction projects in the region, we are also facing some delays. Please see our updated timeline below.

Budget

Capital Investment:

\$22,500,000

Does not include soft costs such as taxes, contingency, & consulting fees.

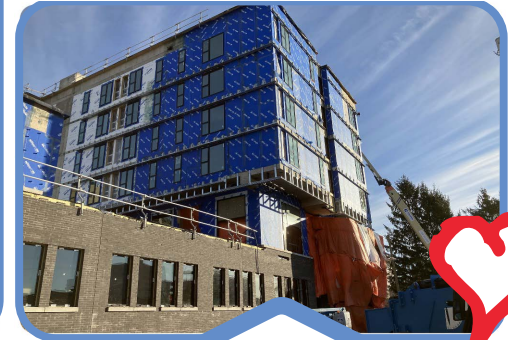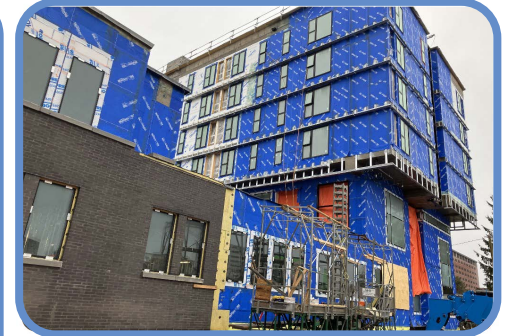

Projected Timeline

June 2022
We broke
ground!

Nov. 2023
Concrete structure
complete

Apr. 2024
Final painting, flooring
and finishes

Spring 2024
Turn over to
RMHC Atlantic

July 2023
2nd floor structure
complete

Dec. 2023
Exterior wall studs
complete

May. 2024
Testing and
commissioning

70%

towards the completion of the
NEW Ronald McDonald House
